

TENDER PACK

Hyperscale Data Centre, Clonee Phase 3

Roof Drainage Package: siphonic primary and gravity overflow

Invitation to tender | Issue T1 | September 2026

Main contractor	Kilcarra Construction
Location	Clonee, Co. Meath
Package	RD-04 Roof drainage (design, supply, install, test)
Return date	Friday 16 October 2026, 12:00
Design standard	BS EN 12056-3:2000, 1 in 100 year storm, 2.5 min
Total roof area	18,170 m2 across 6 roof areas
Documents	38 pages: ITT, drawing list, drawings, specification


*This file is an extract of the tender pack (pages 1, 4, 17 and 22 of 38) for demonstration.
Demo data. Project, quantities and contractor are illustrative.*

Drawing list

Number	Title	Rev
RP-200	Roof general arrangement, key plan	C2
RP-201	Roof plan, drainage zones A to F	C3
RP-202	Roof plan, plant deck (Roof D)	C1
RP-210	Roof falls and gutter setting-out	C2
RP-220	Gutter sections and outlet sumps	C1
RP-230	Parapet overflow details	P2
SE-301	Steel frame, high-level purlin grid	C4
SE-310	Composite deck fixing zones	C1
ME-401	Data hall services coordination, level 03	P3
ME-402	Below-ground drainage connections	C2
AR-501	Elevations, rainwater stack positions	C1
SP-RD04	Specification, roof drainage (section 5.4)	T1

Drawings issued via the main contractor's CDE. Quote drawing numbers and revisions on all RFIs.

RP-201 Roof plan, drainage zones A to F

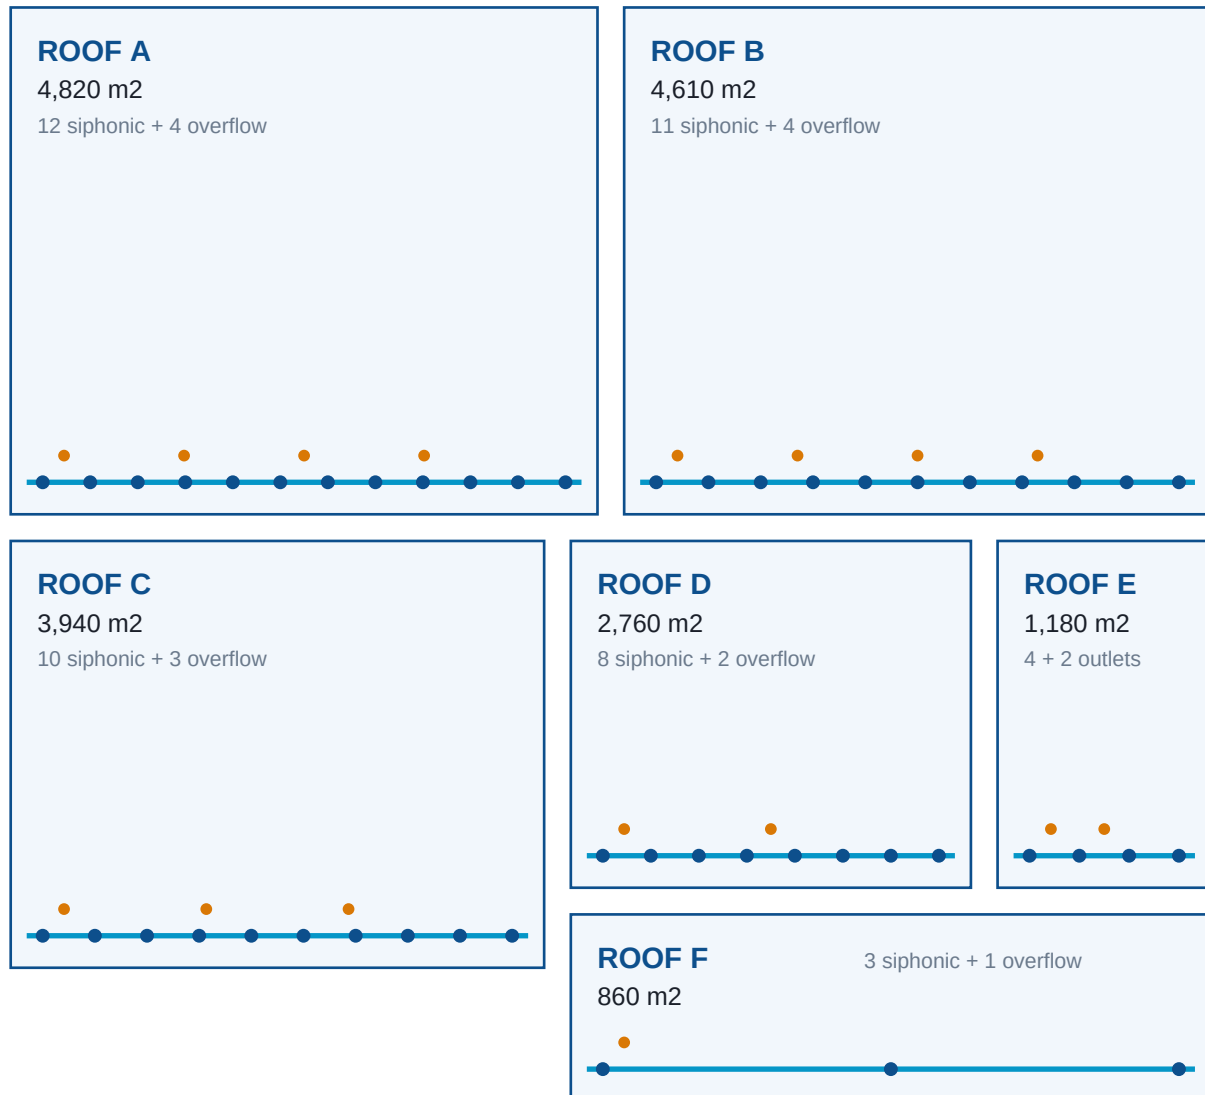

Legend

- Siphonic outlet (48 nr)
- Gravity overflow outlet (16 nr)
- Box gutter

Total roof area 18,170 m². Falls to gutters 1:60 min. Outlet positions indicative, by specialist.

Scale 1:500 at A1 (not to scale in this extract). North to top of sheet.

RP-201 Rev C3

Drawn: KC design team
Status: For tender

Specification excerpt | Section 5.4 Roof drainage

5.4.1 Scope

Design, supply, install, test and commission a siphonic roof drainage system to roofs A to F, with a separate gravity overflow system discharging to parapet spitters and overflow stacks.

5.4.2 Design standard

Design to BS EN 12056-3:2000 and BS 8490:2007. Design storm: 1 in 100 year return period, 2.5 minute duration, with a 1 in 500 year check on the overflow system. Provide full hydraulic calculations, residual head and velocity at every node.

5.4.3 System

Primary: siphonic, HDPE butt-fused or electrofusion, Geberit Pluvia, Valsir Rainplus or equal approved. Pipe diameters from 56 mm to 315 mm. Horizontal collectors on a proprietary suspension rail system fixed to the high-level purlin grid (SE-301).

5.4.4 Prefabrication

Off-site prefabrication of collector spools is encouraged to reduce work at height.

5.4.5 Testing

Pressure test each stack and collector. Provide commissioning certificates, as-built drawings and O&M manual within 4 weeks of practical completion.

5.4.6 By others

Access equipment (MEWPs) and edge protection by main contractor. Thermal insulation and trace heating to exposed pipework by the mechanical contractor. Below-ground drainage connections by the groundworks contractor.
